








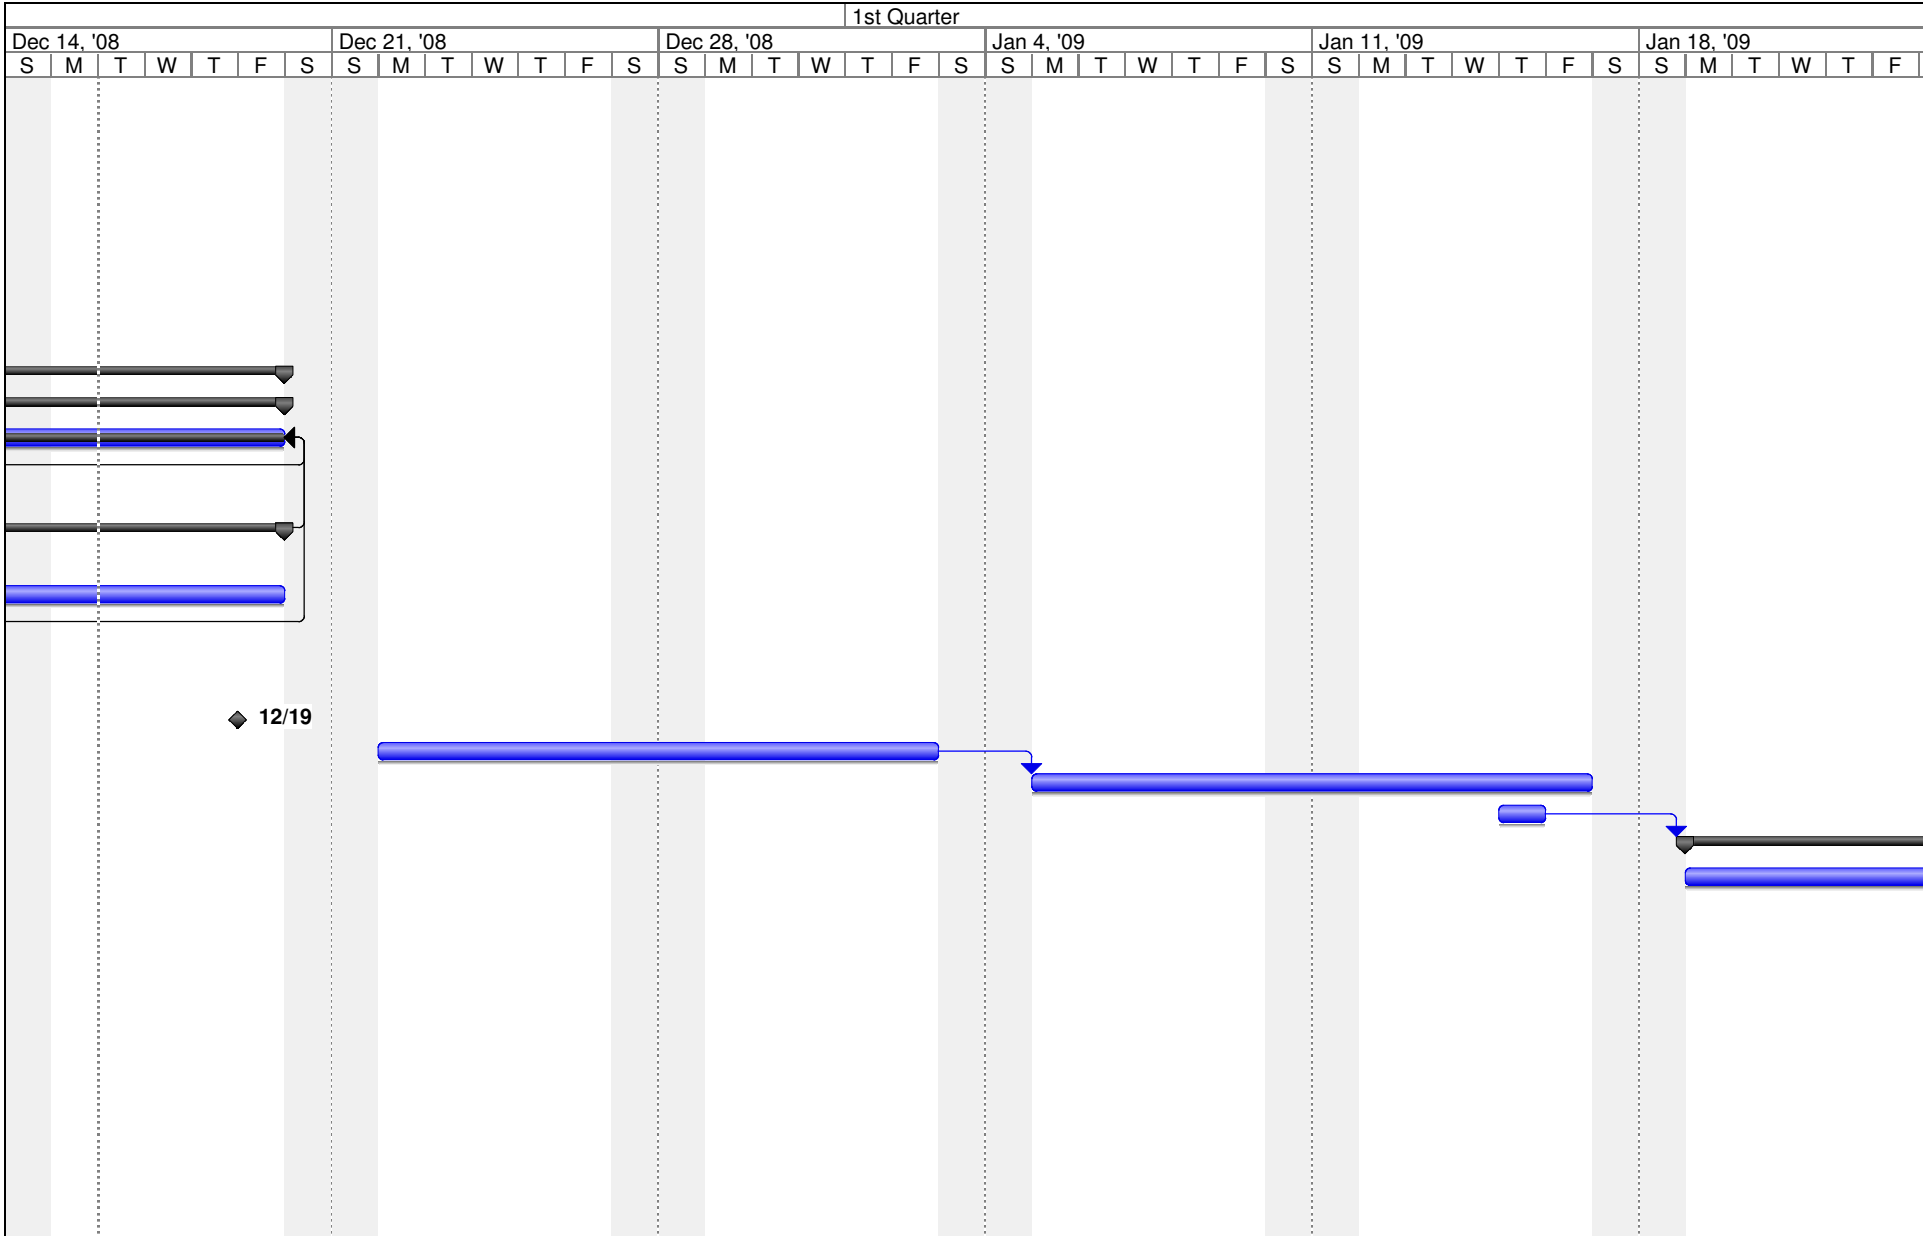


ID	Task Name	Duration	Start	Finish	Predecessors	Nov 30, '08							Dec 7, '08							
						S	M	T	W	T	F	S	S	M	T	W	T	F	S	
1	Start of Winter Quarter	0 days	Mon 12/1/08	Mon 12/1/08																
2	Project Initiation	10 days?	Mon 12/1/08	Fri 12/12/08																
3	Decide Team Name	5 days?	Mon 12/1/08	Fri 12/5/08																
4	Prepare Stakeholder Analysis	5 days	Mon 12/1/08	Fri 12/5/08																
5	Kick-off Meeting	0 days	Thu 12/4/08	Thu 12/4/08																
6	Project Synopsis	2 days?	Thu 12/4/08	Fri 12/5/08	5															
7	Create Team Website	6 days?	Fri 12/5/08	Fri 12/12/08																
8	Project Synopsis Approved	0 days	Fri 12/12/08	Fri 12/12/08																
9	Project Informaiton Survey Completed	0 days	Fri 12/12/08	Fri 12/12/08																
10	Project Planning	12 days?	Thu 12/4/08	Fri 12/19/08																
11	Project integration management	11 days?	Fri 12/5/08	Fri 12/19/08																
12	Development project management plan	11 days?	Fri 12/5/08	Fri 12/19/08	15FF,18FF,13FF															
13	Project Time Management	4 days?	Fri 12/5/08	Wed 12/10/08																
14	Decide on development methodology	4 days?	Fri 12/5/08	Wed 12/10/08																
15	Project Scope Management	12 days?	Thu 12/4/08	Fri 12/19/08																
16	Develop vision & scope statement	2 days?	Thu 12/4/08	Fri 12/5/08																
17	Create WBS and WBS dictionary	11 days?	Fri 12/5/08	Fri 12/19/08																
18	Project Risk Management	4 days?	Fri 12/5/08	Wed 12/10/08																
19	Create Risk Management Plan	4 days?	Fri 12/5/08	Wed 12/10/08																
20	Create Risk Register	2 days?	Fri 12/5/08	Mon 12/8/08																
21	Last Day Before Break	0 days	Fri 12/19/08	Fri 12/19/08																
22	Holiday Break	10 days	Mon 12/22/08	Fri 1/2/09																
23	Sprint 0 (Weeks 4 & 5)	10 days?	Mon 1/5/09	Fri 1/16/09	22															
24	Iteration 1 Planning	1 day?	Thu 1/15/09	Thu 1/15/09																
25	Iteration 1	30 days?	Mon 1/19/09	Fri 2/27/09	24															
26	Sprint 1 (Weeks 6 & 7)	10 days?	Mon 1/19/09	Fri 1/30/09																
27	Sprint 2 (Weeks 8 & 9)	10 days?	Mon 2/2/09	Fri 2/13/09	26															
28	Draft of interim presentation completed	0 days	Fri 2/6/09	Fri 2/6/09																
29	Interim presentation completed	0 days	Fri 2/13/09	Fri 2/13/09																
30	Sprint 3 (Weeks 10 & 11)	10 days?	Mon 2/16/09	Fri 2/27/09	29															
31	Last Day of Winter Quarter	0 days	Fri 2/20/09	Fri 2/20/09																
32	Technical report completed	0 days	Fri 2/27/09	Fri 2/27/09																
33	Winter/Spring Break	5 days	Mon 3/2/09	Fri 3/6/09	30															
34	First Day Spring Quarter	0 days	Mon 3/9/09	Mon 3/9/09																
35	Iteration 2	30 days?	Mon 3/9/09	Fri 4/17/09	34															
36	Sprint 4 (Weeks 1 & 2)	10 days?	Mon 3/9/09	Fri 3/20/09																
37	Sprint 5 (Weeks 3 & 4)	10 days?	Mon 3/23/09	Fri 4/3/09	36															

Project: project-schedule Date: Tue 12/16/08	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	


ID	Task Name	Duration	Start	Finish	Predecessors	Nov 30, '08							Dec 7, '08						
						S	M	T	W	T	F	S	S	M	T	W	T	F	S
						38	Sprint 6 (Weeks 5 & 6)	10 days?	Mon 4/6/09	Fri 4/17/09	37								
39	Iteration 2 Review / Iteration 3 Planning	1 day?	Thu 4/16/09	Thu 4/16/09															
40	Iteration 3	25 days?	Mon 4/20/09	Fri 5/22/09															
41	Sprint 7 (Weeks 7 & 8)	10 days?	Mon 4/20/09	Fri 5/1/09															
42	Sprint 8 (Weeks 9 & 10)	10 days?	Mon 5/4/09	Fri 5/15/09	41														
43	Sprint 9 (Week 11)	5 days?	Mon 5/18/09	Fri 5/22/09	42														
44	Final Iteration Review	1 day?	Thu 5/21/09	Thu 5/21/09															
45	Last Day Spring Quarter	0 days	Fri 5/15/09	Fri 5/15/09															










Project: project-schedule Date: Tue 12/16/08	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	




Project: project-schedule Date: Tue 12/16/08	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

1st Quarter																																																
Dec 14, '08							Dec 21, '08							Dec 28, '08							Jan 4, '09							Jan 11, '09							Jan 18, '09													
S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S							





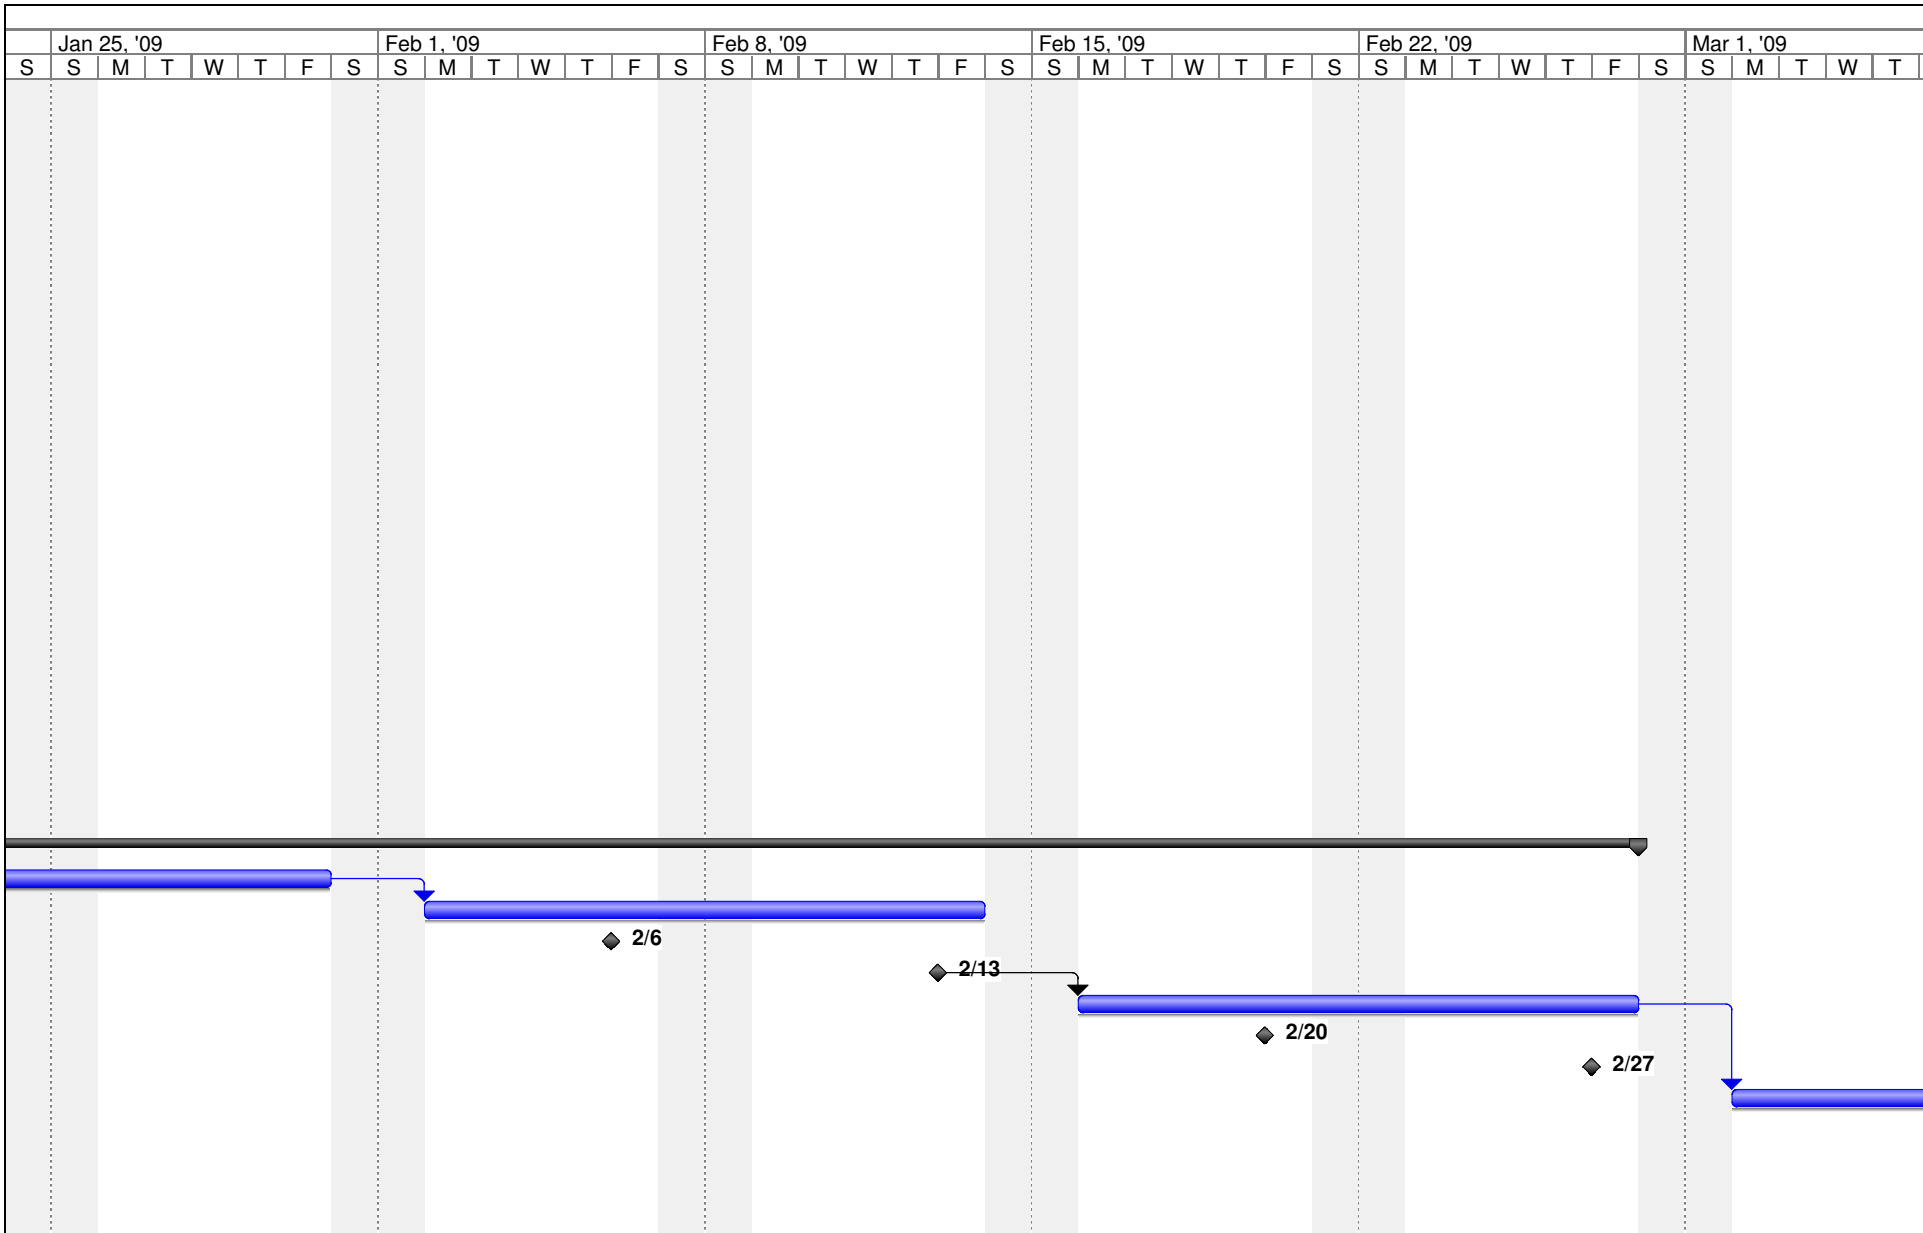






Project: project-schedule Date: Tue 12/16/08	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	




Project: project-schedule Date: Tue 12/16/08	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

Jan 25, '09							Feb 1, '09							Feb 8, '09							Feb 15, '09							Feb 22, '09							Mar 1, '09					
S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T





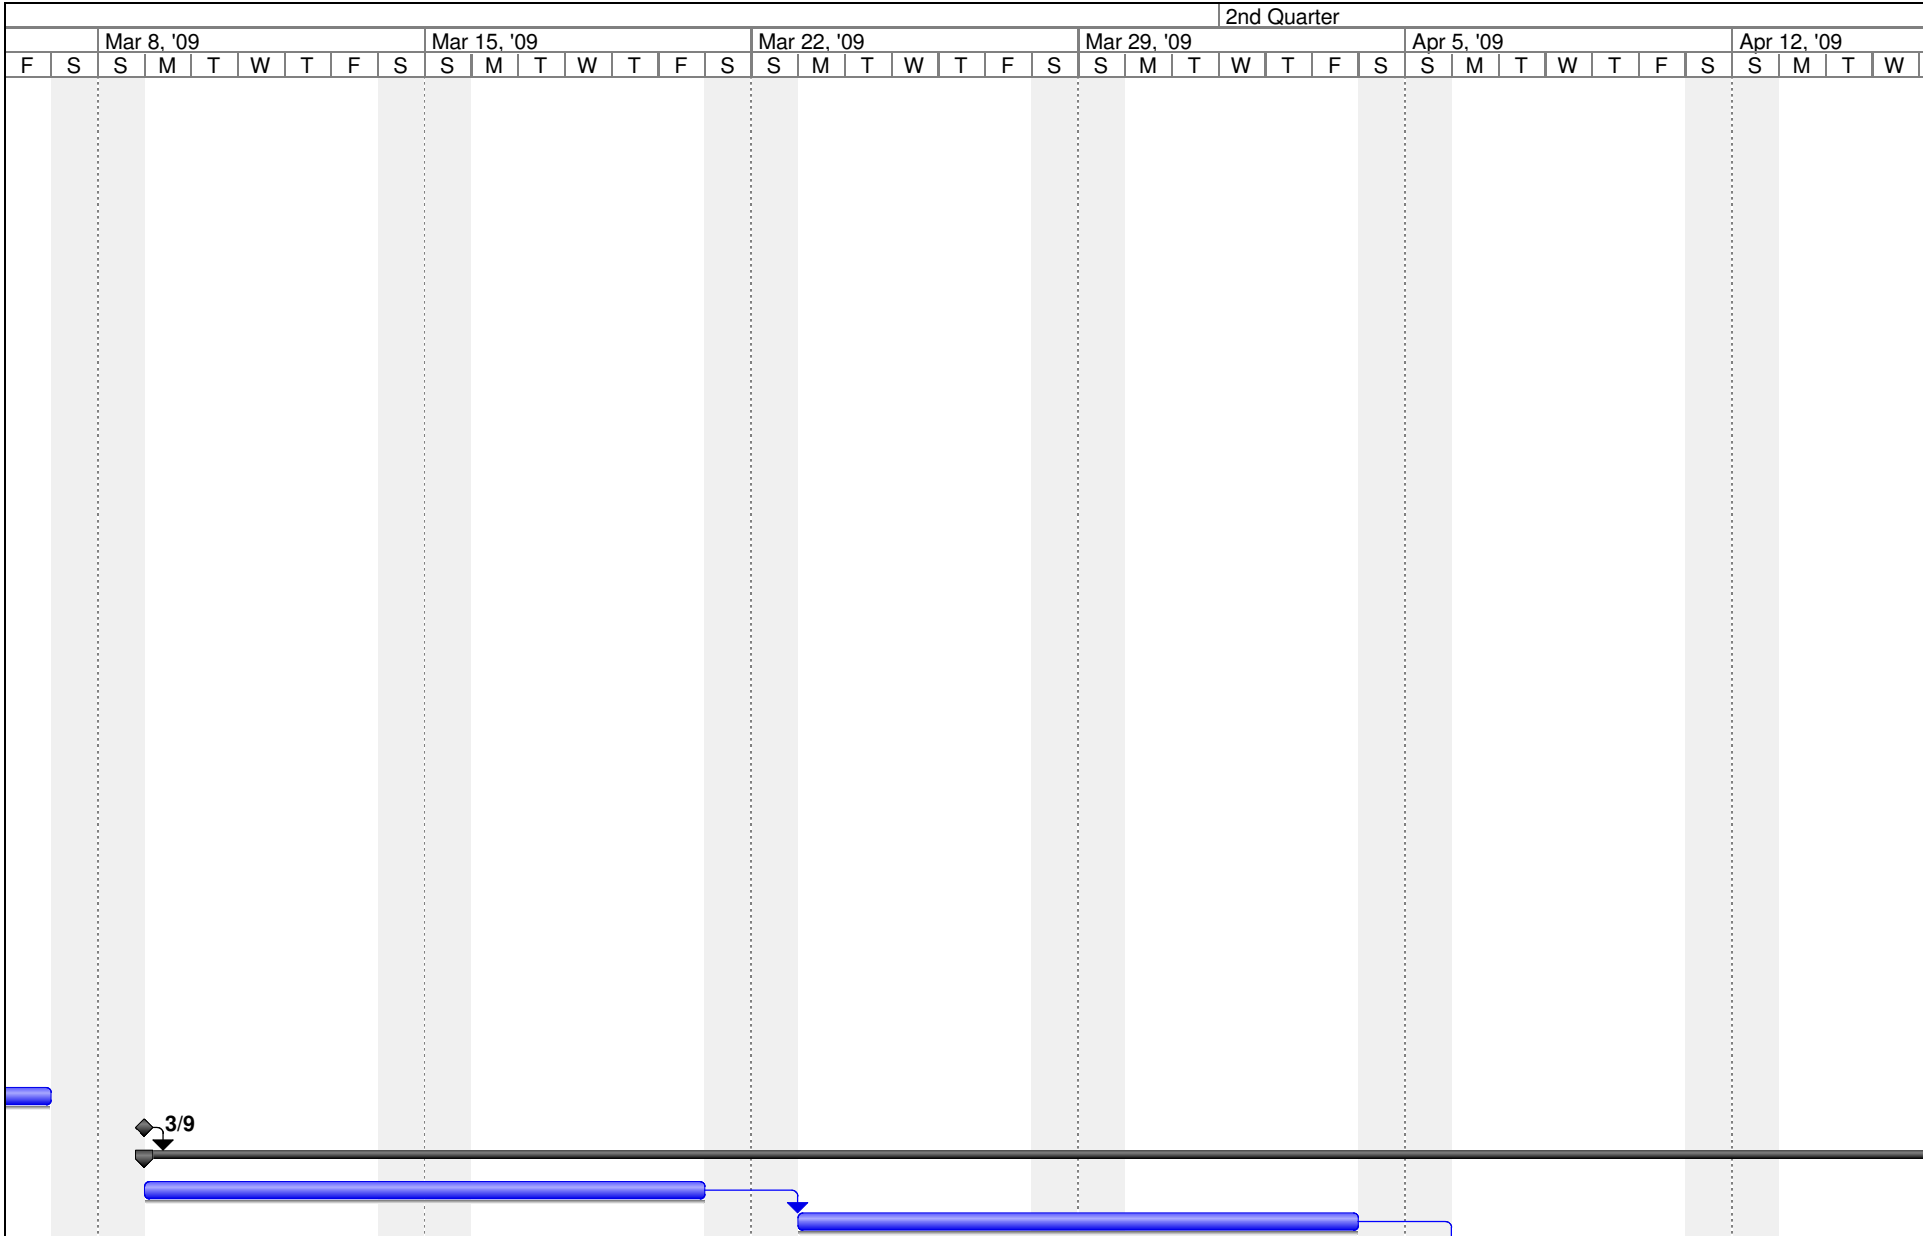






Project: project-schedule Date: Tue 12/16/08	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	




Project: project-schedule Date: Tue 12/16/08	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	


2nd Quarter																																	
Mar 8, '09				Mar 15, '09				Mar 22, '09				Mar 29, '09				Apr 5, '09				Apr 12, '09													
F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W





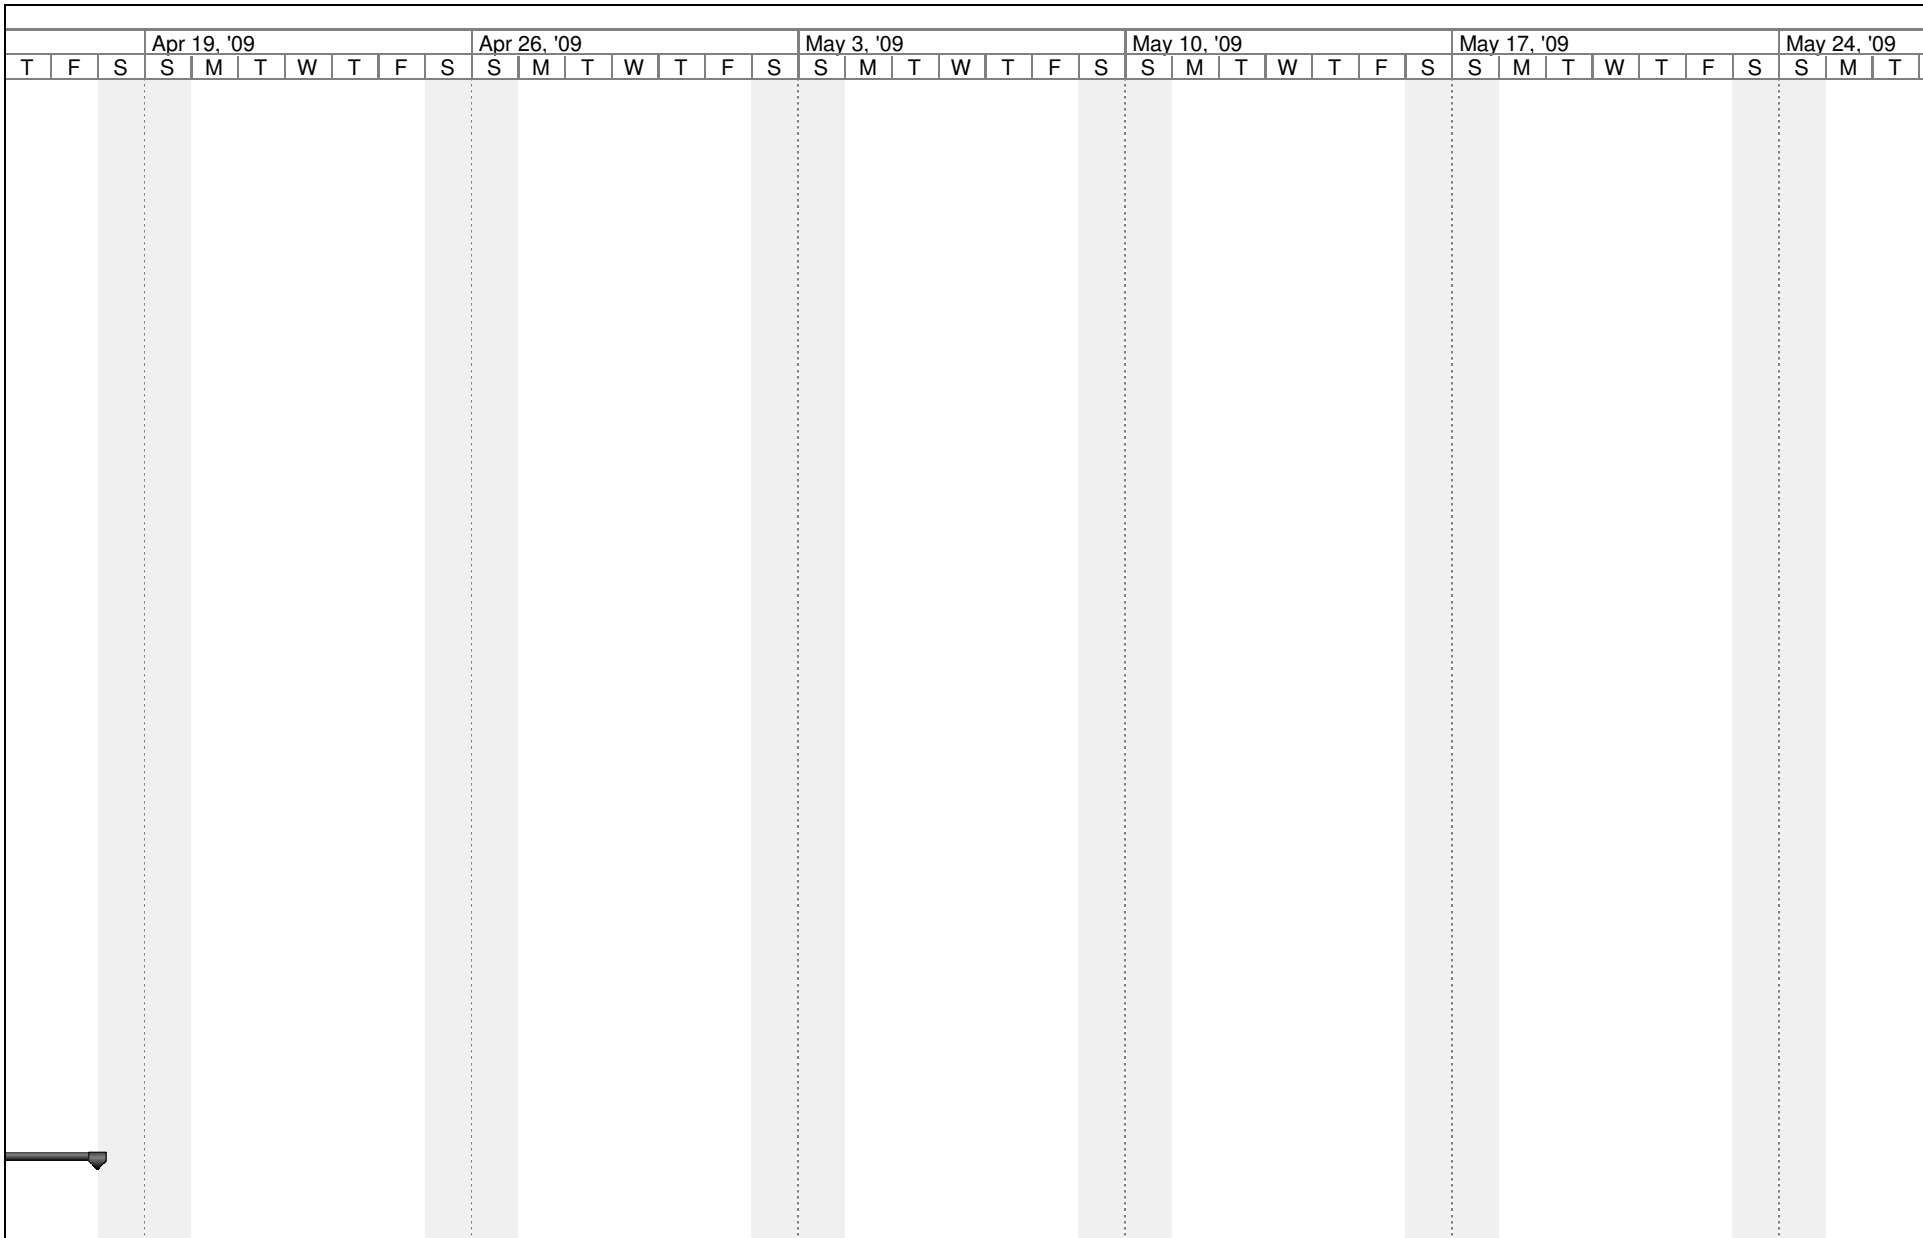



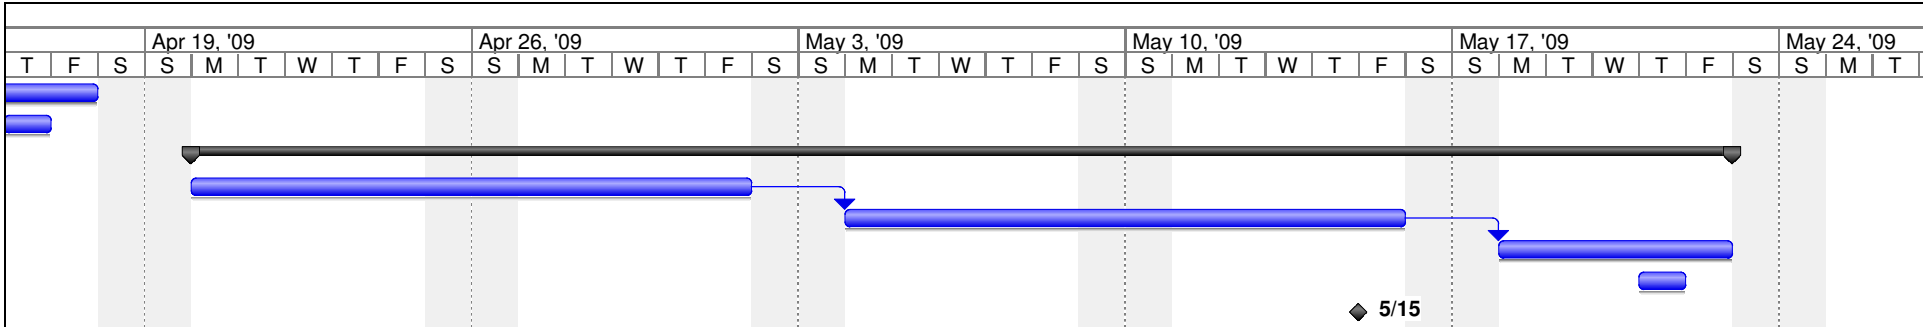

Project: project-schedule Date: Tue 12/16/08	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	



Project: project-schedule Date: Tue 12/16/08	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	



Project: project-schedule Date: Tue 12/16/08	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	
